GLENCORE

BAAL BONE COLLIERY

April to June 2020 Environmental Monitoring Summary



1. Introduction

In accordance with Schedule 5, Condition 9 of Project Approval 09_0178 this report provides a summary of environmental monitoring results for Baal Bone Colliery, for the period **1 April 2020 to 30 June 2020.** Baal Bone's licensed discharge and monitoring locations are identified in **Figure 7**.

2. Air quality

Monthly dust monitoring is carried out in accordance with Australian Standard AS3580.10.1, EPL requirements and Baal Bone's Air Quality Monitoring Program.

Sample analysis is undertaken by the ALS Group Environmental Division, a NATA Accredited laboratory.

Baal Bone maintains a network of dust deposition gauges:

- Sample location DM1 (EPL monitoring point No. 7);
- Sample location DM2 (EPL monitoring point No. 13);
- Sample location DM3 (EPL monitoring point No. 14);
- Sample location DM4 (EPL monitoring point No. 15)

Locations of the dust deposition gauges are shown in Figure 7.

Schedule 3, Condition 10 of Project Approval 09_0178 includes air quality impact assessment criteria for the project and are summarised in **Table 1**. The pollutants to be monitored include deposited dust, TSP and PM¹⁰.

In accordance with the DP&E approved Air Quality Monitoring Program, monitoring for TSP and PM10 was discontinued in June 2012. The monitoring was discontinued following Baal Bone mining operations entering care and maintenance in September 2011, and the completion of coal washing and transporting of coal off-site in December 2011 and April 2012 respectively.

| Pollutant | Averaging period | Criterio | on . |
|----------------|------------------|---------------------------|---------------------------|
| Deposited dust | Annual | Maximum | Maximum |
| | | increase | total |
| | | 2 g/m ² /month | 4 g/m ² /month |
| TSP | Annual | 90 μg/m³ | |
| PM10 | 24 hour | 50 µg/m ³ | |
| | Annual | 30 µg/m ³ | |

Table 1: Baal Bone Air Quality Impact Assessment Criteria

The monthly results for each of the monitoring locations are summarised in

Table 2.

Figure 1 provides the monthly deposited dust results for the year to date. **Figure 2** provides the twelve month rolling average.

| Collection Date | EPL Point 7 DM1 | EPL Point 13 DM2 | EPL Point 14 DM3 | EPL Point 15 DM4 |
|--------------------|--------------------|---------------------|---------------------|---------------------|
| 16-Jan-20 | 6.8 | 7.2 | 8.2 | 12.1 |
| 17-Feb-20 | 2.4 | 4.3 | 3.6 | 3.7 |
| 17-Mar-20 | 1.2 | 1.0 | 1.2 | 0.9 |
| 16-Apr-20 | 0.2 | 0.5 | 0.5 | 0.2 |
| 14-May-20 | 0.7 | 0.7 | 0.7 | 0.7 |
| 15-Jun-20 | 2.0 | 0.2 | 0.2 | 0.3 |

Table 2: Deposited dust monitoring results for 2020 (g/m²/month)

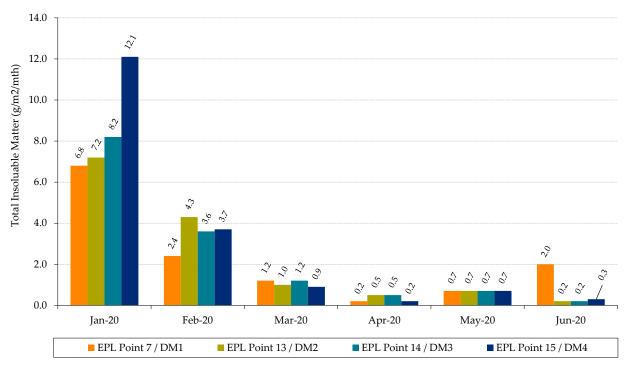


Figure 1: Monthly Total Insoluble Matter

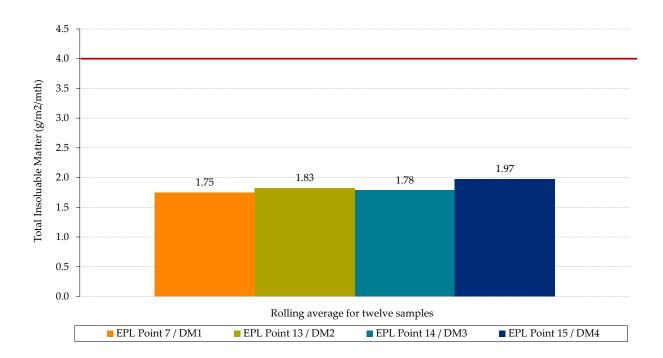


Figure 2: Rolling Average Total Insoluble Matter (12 samples until March 2020)

3. Surface Water

Condition L2 of EPL 765 outlines water concentration limits for oil and grease, pH, total suspended solids and total iron. These limits are presented below in **Table 3**.

| | EPL Monitoring Point 2 (LD2) | EPL Monitoring Point 16 (LDP1) |
|----------------------------------|------------------------------------|--------------------------------------|
| Oil and grease (mg/L) | _ | 10 |
| рН | - | 6.5-8.5 |
| Total Suspended Solids (mg/L) | - | 50 |
| Dissolved Iron (mg/L) | - | 1.0 |

The monthly results for each of the monitoring locations are summarised in

Table 4.

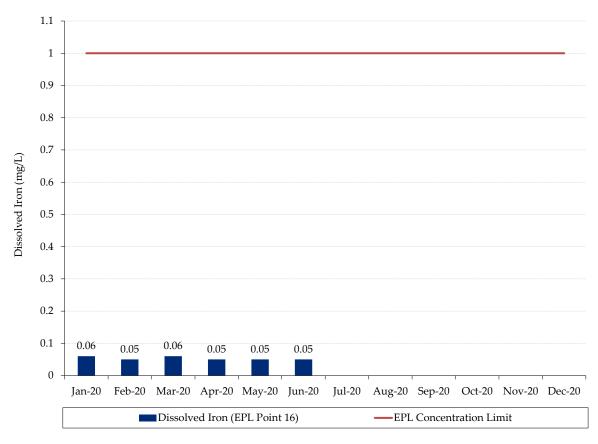


Figure 3 to Figure 6 provide monthly results for each pollutant.

| EPL Point | Month | EC | O&G | SO ²⁻ 4 | Fe | TSS | рН | BOD | Faecal Coliforms | N | Р |
|--------------------------|-------|-------|------|--------------------|------|------|-----|------|---------------------|------|------|
| | | μS/cm | mg/L | mg/L | mg/L | mg/L | - | mg/L | cos/100mls | mg/L | mg/L |
| | Jan | - | _ | _ | - | - | - | - | - | - | - |
| | Feb | - | - | - | - | - | - | - | - | - | - |
| EPL Point | Mar | - | - | - | - | - | - | - | - | - | - |
| 2 (LD2 ^a) | Apr | - | - | - | - | - | - | - | - | - | - |
| $(LD2^{\alpha})$ | May | - | _ | _ | - | - | - | - | - | - | - |
| | Jun | - | - | _ | - | - | - | - | - | - | - |
| | Jan | 1018 | 11 | 370 | 0.06 | <5 | 7.9 | - | - | - | - |
| EDI Deint | Feb | 980 | <5 | 354 | 0.05 | <5 | 6.9 | - | - | - | - |
| EPL Point | Mar | 1025 | <5 | 382 | 0.06 | <5 | 7.3 | - | - | - | - |
| 16 (LDP1) | Apr | 910 | <5 | 344 | 0.05 | <5 | 7.0 | - | - | - | - |
| (LDP1) | May | 885 | <5 | 332 | 0.05 | 6.0 | 6.9 | - | - | - | - |
| | Jun | 932 | <5 | 345 | 0.05 | <5 | 7.2 | - | - | - | - |

Table 4: EPL Water quality results for 2020

Notes (a) No samples taken at LD2 during 2020 to date as sample location was dry

Legend

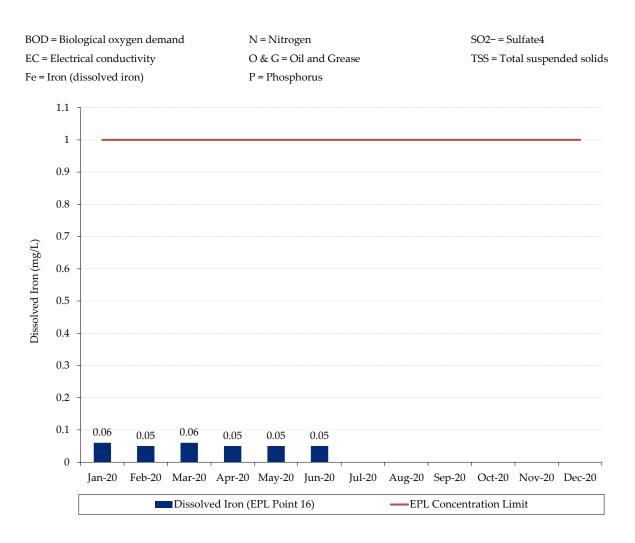


Figure 3: Monthly Dissolved Iron

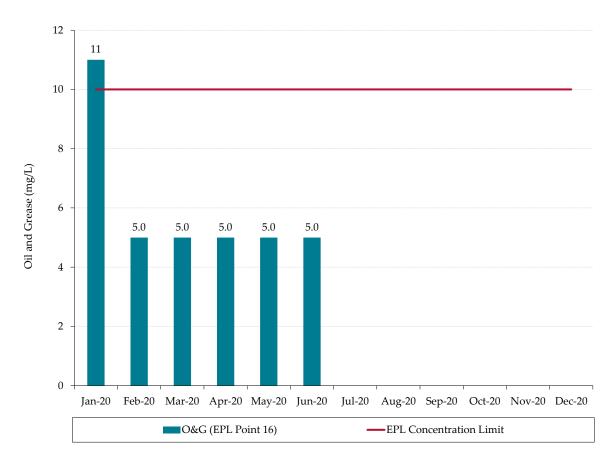


Figure 4: Monthly Oil and Grease

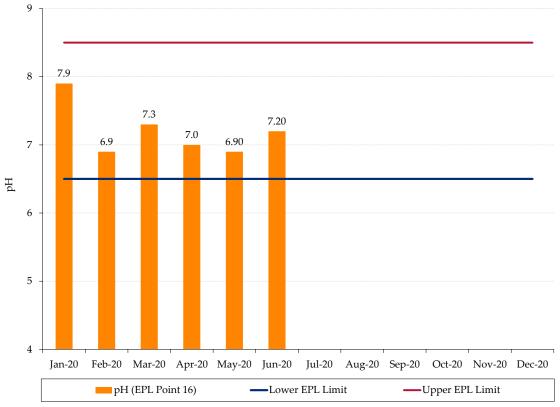


Figure 5: Monthly pH

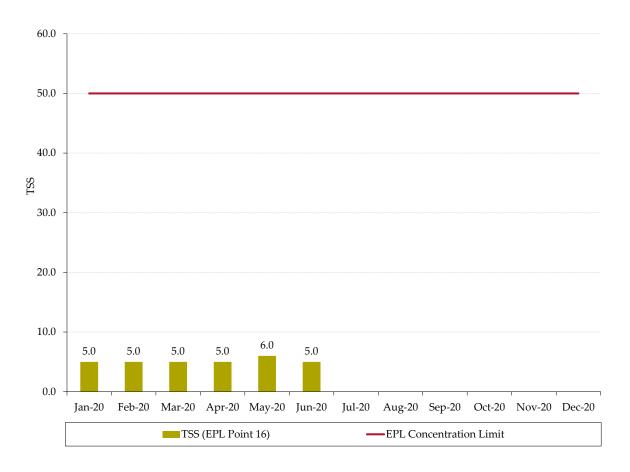


Figure 6: Monthly Total Suspended Solids

A summary of monitoring results for EPL discharge and monitoring points (those with specified concentration limits) can be found below for the period 1 April 2020 to 30 June 2020:

- All dissolved iron samples were well below the concentration limit of 1 mg/L;
- All samples returned pH results that were within the upper and lower EPL limits (8.5 and 6.5 respectively);
- All monthly TSS results were below the EPL concentration limit of 50 mg/L;
- Oil and grease levels were below the EPL concentration limit of 10mg/L.

Note: Oil and grease levels in January 2020 exceeded the EPL concentration limit of 10mg/L, with a result of 11 mg/L. A notification was sent to the Environment Protection Agency and the Department of Planning, Industry and Environment on 24/02/2020 regarding the oil and grease exceedance. An investigation was undertaken into this exceedance which found that potential contributors may have been the extended dry spell and recent rainfall, the bushfires moving through the area as well as vehicles and machinery on site. Oil and grease levels for the period February 2020 to June 2020 were below the EPL concentration limit.

Monthly EPL reporting can be accessed at:

http://www.glencore.com.au/en/who-we-are/energy-products/baal-bone/Pages/eplreporting.aspx

4. Noise

Noise Impact Assessment Criteria

Schedule 3, Condition 4 of Project Approval 09_0178 includes long term noise impact assessment criteria. **Table 5** outlines the assessment criteria.

| Table 5: Long te | rm noise impa | act assessment o | riteria |
|------------------|---------------|------------------|---------|
| rubie of Long te | in noise mipe | | |

| Location | All periods dB(a) L _{Aeq(15 min)} | Night dB(a) LA1(1 min) |
|--------------------------------|---|---------------------------|
| R1 | 46 | 47 |
| R2 | 41 | 48 |
| R3 | 41 | 48 |
| All other privately-owned land | 35 | 45 |

From 2013 onwards attended monitoring is undertaken on an annual basis at receptors R1 and R2/R3, shown in **Figure 7**.

Noise Audit Results

Global Acoustics conducted the annual environmental compliance noise audit at Baal Bone Colliery on Tuesday 25 June 2019 during the day, evening and night periods. The next noise audit is scheduled for mid 2020.

Table 6 to

Table 8 provide a summary of the 2019 noise audit results.

Table 6: Noise Audit Summary (Daytime)

| Location (Start time) | Measured Predicted BBC Noise | Limit | Unit | Comments |
|-------------------------------|------------------------------------|-------|------|---------------|
| | LAeq15min d | B | | |
| Daytime Audit - | – Tuesday 25 June | 2019 | - | _ |
| Location R1 (1447 hours) | 31 | 46 | dB | In compliance |
| Location R1 (1502 hours) | 26 | 46 | dB | In compliance |
| Location R2/3 (1532 hours) | <25 | 41 | dB | In compliance |
| Location R2/3 (1547 hours) | <25 | 41 | dB | In compliance |

Table 7: Noise Audit Summary (Evening)

| Location (Start time) | Measured Predicted BBC Noise | Limit | Unit | Comments |
|-------------------------------|------------------------------------|-------|------|---------------|
| , | LAeq15min d | | | |
| Evening Audit- | Tuesday 25 June | 2019 | | |
| Location R1 (2052 hours) | 27 | 46 | dB | In compliance |
| Location R1 (2107 hours) | 26 | 46 | dB | In compliance |
| Location R2/3 (2132 hours) | <25 | 41 | dB | In compliance |
| Location R2/3 (2147 hours) | <25 | 41 | dB | In compliance |

Table 8: Noise Audit Summary (Night)

| Location (Start time) | Measured Predicted BBCNoise | Limit | Unit | Comments |
|-------------------------------|-----------------------------------|-------|------|---------------|
| | LAeq15min d | В | | |
| Night Audit– Ti | uesday 25 June 20 | 19 | | |
| Location R1 (2242 hours) | <25 | 46 | dB | In compliance |
| Location R1 (2257 hours) | <25 | 46 | dB | In compliance |
| Location R2/3 (2202 hours) | <25 | 41 | dB | In compliance |
| Location R2/3 (2217 hours) | <25 | 41 | dB | In compliance |

The audit report concluded that:

"Attended monitoring was conducted in accordance with relevant EPA guidelines and Australian Standard AS 1055 'Acoustics, Description and Measurement of Environmental Noise'. The duration of each measurement was 15 minutes. The survey purpose is to quantify and describe the existing acoustic environment around BBC and compare results with relevant limits.

Noise levels from BBC complied with the LAeq,15minute and LA1,1minute development consent criteria at all monitoring locations during the June 2019 survey."

The full July 2019 audit report and previous noise audit reports can be accessed from the Baal Bone publications web page at:

http://www.glencore.com.au/en/who-we-are/energy-products/baal-bone/Pages/eplreporting.aspx

